Project Plan

EventMaster

Industry Partner	
Primary Instructor	Laily Ajellu
Team Member	Steven Coverdale

Team Member	Jaeden Salandanan
Team Member	Vincent Luu
Team Member	Regina Slonimsky
Team Member	

Document Revision History

Revision #	Date
1.0.0	October 24, 2025
2.0.0	February 8, 2026

Table of Contents

Contents

1. Executive Summary..... 4

2. Project Approvers, Reviews and Distribution List..... 4

3. Scope..... 5

4. Deliverables..... 6

5. Assumptions..... 6

6. Dependencies..... 6

7. Risk Management..... 7

8. Communication..... 7

9. Task Listing (WBS- Work Breakdown Structure)..... 8

10. Gantt Chart..... 9

11. Milestones..... 9

12. RAM – Responsibility Assignment Matrix..... 9

13. Approval..... 10

1. Executive Summary

The following describes the project to be executed.

Objective	The Objective here is to design and develop a web-based ticketing platform that simplifies event experiences for organizers and attendees through secure, intuitive and transparent tools.
Corporate Goals Addressed	Promote innovation in digital commerce and event management
Planned Start Date	Jan 2026
Planned End Date	April 2026

2. Project Approvers, Reviews and Distribution List

Approvers, reviewers and distribution list

Project Role	Name	E-mail	Date
Project Manager/Lead	Steven Coverdale	Steven.coverdale@gmail.com	Oct 2025
Frontend Developer	Regina Slonimsky	regina.slonimsky@hotmail.com	Oct 2025

Backend Developer	Jaeden Salandanan	jaeden_salandanan@yahoo.com	Oct 2025
QA Specialist	Vincent Luu	luu.vincent11@gmail.com	Oct 2025

3. Scope

Define the sum total of all of its products and their requirements or features.

In Scope	Out of Scope
User Registration & Authentication	Native Mobile App
Event Creation & Management	Payment Gateway
Ticket Browsing, Selection & “Purchase”	Multi-Language support
Admin Dashboard	Fraud detection
Basic Consumer support	QR Code generation
	External Marketing Platform

4. Deliverables

This project will deliver the following.

Deliverable	Description (Task Breakdown)
Web-Based ticketing	A responsive ASP.NET Core MVC application that’ll allow users to browse events, purchase tickets and even manage user accounts. This is the core deliverable **Event Browsing Interface** Build responsive pages for event listings, filtering, and event detail views.

	Detail page with title, description, Date/Time/Venue/ Price and image/banner Filtering will be simple (no advanced search logic) Once image per event is enough for MVP (Maybe theme too) **Ticket Purchase Flow** Implement seat selection, pricing breakdown, checkout, and confirmation pages. No seat maps No Real Payment integration(Swipe is our main goal) Email Confirmation **User Account Management** Create profile pages, order history, saved events, and account settings
Event Management Dashboard	Organizer facing interface for creating events, tracking ticket sales, viewing analytics and managing logistics Saved/Favorited events Simple UI **Event Creation/Editing Tools** Forms and workflows for organizers to create events, upload media, set pricing, and configure schedules No multiday scheduling No complex pricing tiers One price per event **Sales/Attendance Analytics** Charts, tables, and insights showing revenue, ticket sales, and attendance trends Simple tables/numbers Charts **Logistics Panel**

	Tools for managing capacity, validation, admin permissions, and event operations
User registration & authentication	Secure login and account creation system for both attendees and organizers with role-based access control QR Code scanning will be out of scope Manage event visibility(Publish/Unpublish) **Role-Based Access Control** Identify attendee, organizer, and admin permissions respectively. Two roles just for the MVP. Should expand for Organizer's staff **Secure Login/Signup** Implement email/password authentication, password reset, and validation flows Social Login however no 2FA **Security Layer** SSL, CPPA-aligned data handling, session management, and secure storage of user credentials
Basic Consumer support	FAQ, implement form for customer support No ticketing system or Live chat…
Transparent pricing	Visual Breakdown of ticket costs, service fee and organizer-defined pricing structures Fee calculator with no dynamic fee rules.

5. Assumptions

This project makes the following assumptions;

1. Users are familiar with basic web navigation and online purchasing workflows
2. Organizers have access to event metadata

3. Admins and organizers will actively monitor dashboards
4. Users expect industry standard data protection
5. Organizers have event metadata and will use dashboards
6. Users will have access to modern web browsers
7. Payment simulations are acceptable for MVP
8. Stakeholders will provide feedback during development
9. Platform will be hosted securely and comply with Canadian privacy laws
10. Users provide real and accurate information when registering
11. Mobile app development is not in scope for the time frame given

6. Dependencies

The successful delivery of EventMaster relies on several internal and external dependencies. These factors must be acknowledged early to ensure proper planning, risk mitigation, and realistic expectations throughout the development time.

Internal

- Team availability
  - Consistent participation
  - Scheduling alignments for meetings, coding sessions
- Technical skills
  - C3, ASP.NET, Core MVC and Entity Framework Core
  - Ability to implement CRUD operations and MVC patterns
  - Comfort with front end tech (HTML, CSS, Bootstrap)
  - Learning curve (Email, Charts, File Uploads)
- Project artifacts
  - Wireframe docs
  - Database schema
  - API Design Specs
  - Testing plans/QA Checklist
- Design decisions
  - Pricing models
  - Defining roles and permissions
- Testing QA
  - Time allocated for functioning testing
  - Browser testing (Chrome, Edge, Firefox)
  - Validation forms, authentication and event workflows
  - Bug fixing
- Documentation Quality
  - Clear technical documentation for instructors
  - User guide for navigating the platform
  - API Documentation
  - Final Project Report

External

- WebHosting
  - Deployment environment
  - Configuration of hosting settings, database connections and SSL
- Third-party payment
  - Mock payment flow
  - Simulated API endpoints
  - Stable logic for checkout and confirmation
- Browser Compatibility
  - Ensuring the platform works on major browsers
  - Responsive design for mobile and desktop
- Internet access
  - Hosting
  - Email Delivery
  - External API calls (Maps & mock Payment)
- Regulatory Compliance
  - Basic alignment with CPPA principles
  - Secure storage of user credentials
  - HTTPS enforcement on deployment
- Email delivery service
  - Integration with SendGrid
  - Dependency on external service confirmations

7. Risk Management

The following outlines key risks associated with the development of EventMaster, along with their severity likelihood and the strategies we will use to manage or mitigate them

Potential Risk	Severity (H/M/L)	Likelihood (H/M/L)	Management Strategy
Limited budget for advanced features	H	H	Focus on core MVP, Document deferred features for future implementation
Time Constraints to due semester deadlines	H	H	Need to prioritize essential features, use agile sprints and early testing cycles
Small team	M	M	Assign clear roles, use modular design to parallelize tasks
Third party API	M	M	Use Sandbox environments, document fallback strategies
Regulatory compliance	M	M	Follow best practices for data protection, limit scope of personal data

Browser Compatibility	L	M	Test on all major browsers(Chrome, Firefox, Edge)
Delayed stakeholder feedback	M	M	Schedule regular check-ins, Use mockups and demos for early validation
Security vulnerabilities	H	M	Implement SSL/Token-based authentication and secure hosting, Avoid storing sensitive data such as keys
Scope creep from feature requests	M	M	Lock scope early, use a formal change request process
Performance bottlenecks under load	H	M	Load test critical work flows like checkout and login, optimize queries
Data loss or corruption	H	L	Backup database regularly, use versioned deployments

8. Communication

Reporting

The following reports will be produced;

Report	Audience	Frequency
Weekly Progress Report	Project Team, Instructor	Weekly(Sunday Latest)
Sprint Review Summary	Project Team, Instructor	End of each sprint
Meeting Minutes	Project Team, Instructor	After each meeting
Feature Status Tracking	Project Team	Updated weekly
Bug and issues	Project team	Continuous
Final Report	Project Team, Instructor	End of April

Stakeholder feedback	Project Team, Instructor	Mid-project & Final

Meetings

The following meetings/communication will be established;

Meeting	Purpose	Attendees	Frequency
Weekly Standups	Share Progress/Blockers	Project Team	Monday Morning
Sprint Planning	Define our goals, assign tasks	Project Team	Monday Morning (Bi-weekly)
Sprint Review	Showcase completed features and gather feedback	Project Team	Monday Morning (End of Sprint)
Design review	Finalize UI/UX	UI/UX Team	As needed
Technical Sync	Resolve integration issues and align on architecture decisions	Project Team	As needed
Product truth	Present progress and gather feedback.. make sure product is coming together	Project Team, Instructor	Every two sprints

9. Task Listing (WBS- Work Breakdown Structure)

The following resource proposal template summarizes the resource hours committed to this project, upon final approval of this document.

Ref	Task	Details	Duration	Dependency	Priority
1.0	Requirements Gathering & Analysis	Define scope, user roles, features, and constraints. Document assumptions and dependencies.	5 days	—	High
2.0	UI/UX Design	Create wireframes, mockups, and accessibility-compliant layouts for all major user flows. (Attendee + Organizer)	10 days	1.0 Requirements	High
3.0	Database Schema Design	Design relational schema for users, events, tickets, and admin analytics. Normalize and document relationships.	5 days	1.0 Requirements	High
4.0	User Authentication Module	Implement registration, login, session management, and role-based access using ASP.NET Identity.	5 days	3.0 Database Schema	High
5.0	Event Creation & Management	Build organizer tools for creating, editing, and tracking events. Include metadata, pricing and capacity settings.	10 days	3.0 Database Schema	High
6.0	Ticket Browsing & Purchase Flow	Develop user-facing ticket search, event detail pages, ticket selection, and simulated checkout flow	10 days	4.0 Authentication, 5.0 Event Management	High
7.0	Admin Dashboard & Analytics	Create dashboards for event metrics, ticket sales, and user activity. Include basic visualizations. (Tables or charts)	10 days	5.0 Event Management	Medium
8.0	Consumer Support Interface	Build FAQ, contact form, and basic support ticket submission workflow.	5 days	6.0 Ticket Purchase	Medium

Ref	Task	Details	Duration	Dependency	Priority
9.0	Pricing Breakdown & Fee Calculator	Implement transparent pricing logic with a breakdown of base price, service fees, and taxes.	5 days	6.0 Ticket Purchase	Medium
10.0	Security Implementation (SSL, 2FA)	Add HTTPS, token-based auth, and optional two-factor authentication.	5 days	4.0 Authentication	High
11.0	Testing & QA	Perform functional, usability, and edge-case testing across all modules. Log and resolve bugs.	10 days	All development tasks	High
12.0	Final Presentation & Documentation	Prepare final report, presentation deck, and demo walkthrough for submission.	5 days	11.0 Testing & QA	High

10. Gantt Chart

Create a detailed Gantt Chart from your Task Listing(Use any software tool and paste the image or upload as a separate file that can be opened as pdf/doc/xls)

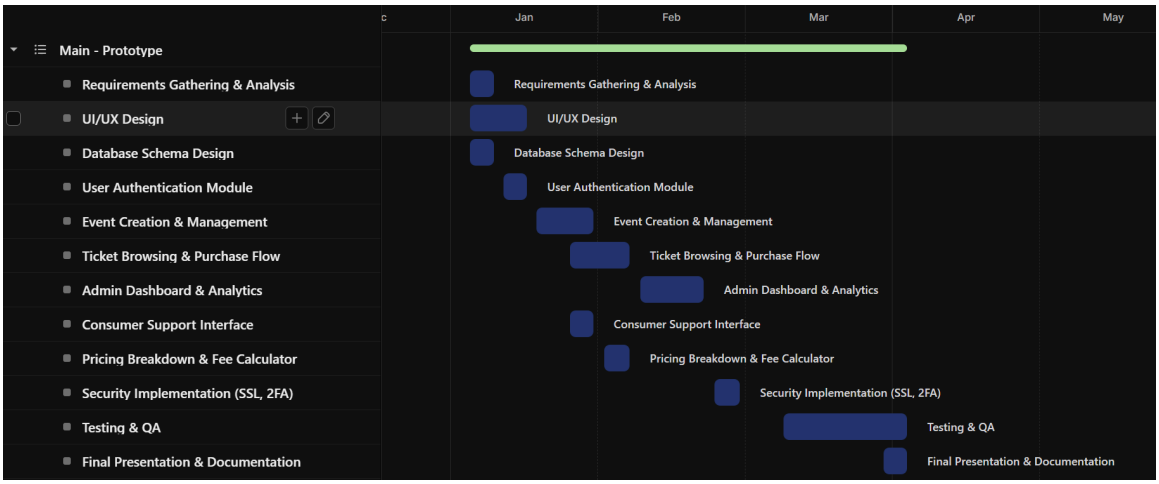

11. Milestones

Major Activity or Milestone	Estimated Milestone Target date	Owner/Reviewer Team Members
Milestone 1 – Planning & Design	Week 4	Finalize requirements, UI/UX wireframes, database schema, WBS approval
Milestone 2 – Core Development	Week 8	Authentication, event creation, ticket browsing, basic dashboard
Milestone 3 – Feature Completion & QA	Week 12	Pricing breakdown, Consumer Support, Security & Full QA Pass
Milestone 4 – Final Delivery & Presentation	Week 16	Final Report, Demo-ready build, Presentation deck + Instructor Signoff

12. RAM – Responsibility Assignment Matrix

Create a RAM from your Task Listing. A sample is shown below:

Task	Steven (PM/Lead)	Regina (Frontend)	Jaeden (Backend)	Vincent (QA/Support)
Requirements Gathering & Analysis	P	S	S	S

UI/UX Design	S	P	-	S
Database Schema Design	S	-	P	S
User Authentication Module	S	-	P	S
Event Creation & Management	S	P	-	S
Ticket Browsing & Purchase Flow	S	P	-	S
Admin Dashboard & Analytics	S	P	-	S
Consumer Support Interface	S	-	-	P
Pricing Breakdown & Fee Calculator	S	-	-	P
Security Implementation (SSL, 2FA)	S	-	P	-
Testing & QA	S	-	-	P
Final Presentation & Documentation	P	P	P	P
	P/2 – S/10	P/5 – S/1	P4/ - S/1	P/4 – S/7

13. Approval

The signatures below indicate their approval of the contents of this document.

Project Role	Name	Signature	Date

Project Manager/Lead	Steven Coverdale	StevenCoverdale	Feb 15th 2026
Frontend Developer	Regina Slonimsky	Regina Slonimsky	Feb 15th 2026
Backend Developer	Jaeden Salandanan	Jaeden Salandanan	Feb 15th 2026
QA Specialist/Support	Vincent Luu	Vincent Luu	Oct 26th 2025
